

Gipson Construction

2272 Moores Mill Road, Suite 201
Auburn, AL 36830
(800) 700-8321
<http://gipsongc.com>




The Preserve Lot #3

Project Log Report

Monday, January 23, 2023

Weather Conditions

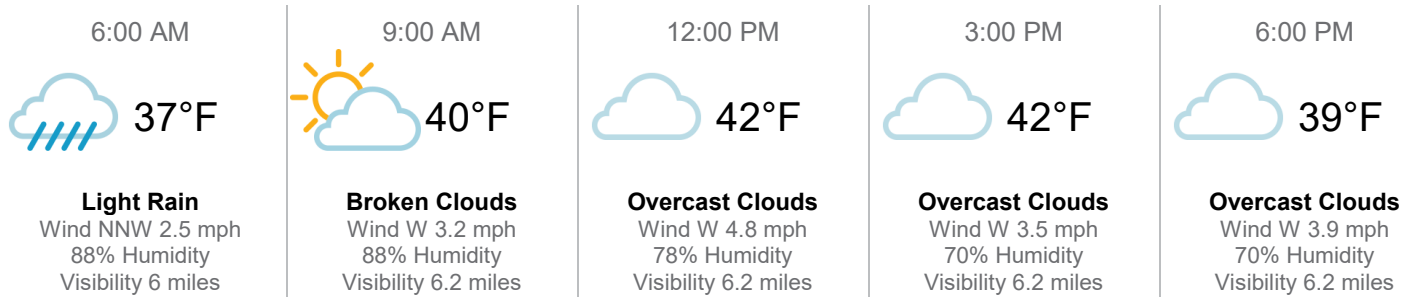

Materials

Name	QTY	Cost	Total	Description	Time Posted
Drywall General Requirements	1	\$ 7,560.00	\$ 7,560.00		01/26/2023 9:25:02 AM - Alex Honbarrier

Delivery Log

Attachments:





Resource	Delivery Duration	Delivery Details	Time Posted
Luis Caracas Caracas Contractors	9:15 AM - 10:15 AM	Interior office doors from West Pac. inspected by Alex	01/26/2023 9:28:32 AM - Alex Honbarrier

Custom Delays

Posted By	Delay Duration	Description	Time Posted
Alex Honbarrier Gipson Construction	9:00 AM - 5:00 PM	Thomas Green - Handrail fabrication postponed due to his sickness.	01/26/2023 9:32:44 AM - Alex Honbarrier

Tuesday, January 24, 2023


Weather Conditions


6:00 AM	9:00 AM	12:00 PM	3:00 PM	6:00 PM
 33°F	 41°F	 46°F	 47°F	 37°F
Clear Sky Wind SW 1 mph 76% Humidity Visibility 6.2 miles	Clear Sky Wind SW 2.6 mph 57% Humidity Visibility 6.2 miles	Clear Sky Wind W 3.2 mph 46% Humidity Visibility 6.2 miles	Clear Sky Wind W 2.9 mph 44% Humidity Visibility 6.2 miles	Clear Sky Wind W 0.3 mph 70% Humidity Visibility 6.2 miles


Work Log

Resource	Showed	Workers	Hours	Description	Time Posted
Sam Creed Gipson Construction Construction Manager	Yes	5	8	<ul style="list-style-type: none">- Performed a walk-through of work done inside so far with Korey.- Assembled air manifold and air dryer piping. We'll need the horizontal electrical raceway on the wall to be removed by Grainger first before we can install them.-Ran one 1/2" air line to dispenser control panel area.- Installed router and IT cabinet in maintenance shop area.	01/26/2023 9:32:29 AM - Alex Honbarrier

Attachments:

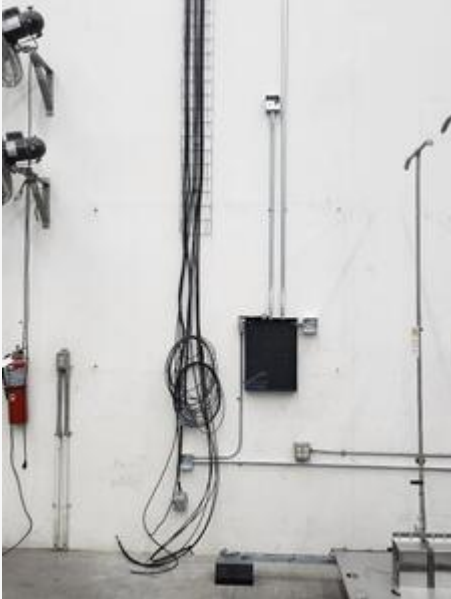





Project Notes





Posted By	Project Note	Time Posted
Alex Honbarrier Gipson Construction	I sketched up the stairwell last night. If we want to maintain the space under the stairs in the bedroom we will need a post or some means of hanging the platform off the beam to make the turn. Also the clip in the hallway looks inevitable. Looking for some feedback here before either release the guys in this area.	01/26/2023 9:27:26 AM - Alex Honbarrier

Safety Log

Resource	Type & Time	Description	Compliance Due	Time Posted
Wesley Belvedere Fargo Lumber	Accident 8:15 AM	Trip and fall on-site; bruising but no breaks		01/26/2023 9:27:15 AM - Alex Honbarrier

Wednesday, January 25, 2023

Weather Conditions

<p>6:00 AM</p>  <p>34°F</p> <p>Clear Sky Wind E 1.9 mph 78% Humidity Visibility 6.2 miles</p>	<p>9:00 AM</p>  <p>36°F</p> <p>Overcast Clouds Wind ENE 1.6 mph 76% Humidity Visibility 6.2 miles</p>	<p>12:00 PM</p>  <p>36°F</p> <p>Moderate Rain Wind ENE 1.6 mph 86% Humidity Visibility 5 miles</p>	<p>3:00 PM</p>  <p>41°F</p> <p>Light Rain Wind ENE 2.2 mph 93% Humidity Visibility 2 miles</p>	<p>6:00 PM</p>  <p>48°F</p> <p>Overcast Clouds Wind E 1.6 mph 90% Humidity Visibility 2 miles</p>
---	--	---	--	--

Observed Weather & Delays

Posted By	Delay Duration	Description	Time Posted
Alex Honbarrier Gipson Construction	12:00 PM - 2:00 PM	heavy rain	01/26/2023 9:26:36 AM - Alex Honbarrier

Visitor Log

Resource	Visit Duration	Type	Reason For Visit	Time Posted
Matt Shulker Harp Drywall	11:00 AM - 11:30 AM	Drywall		01/26/2023 9:30:53 AM - Alex Honbarrier
Doug Andrews Homeowner	9:45 AM - 10:15 AM	Client		01/26/2023 9:30:18 AM - Alex Honbarrier
